


# ASMAB Progress Chart 3 August 2009

\* the projected substantial completion date for main building (incl. landscape & signs) is by end aug. '09  
 \* the projected completion date for telescope maintenance room is by end dec. '09

— contract  
 — actual  
 — rate

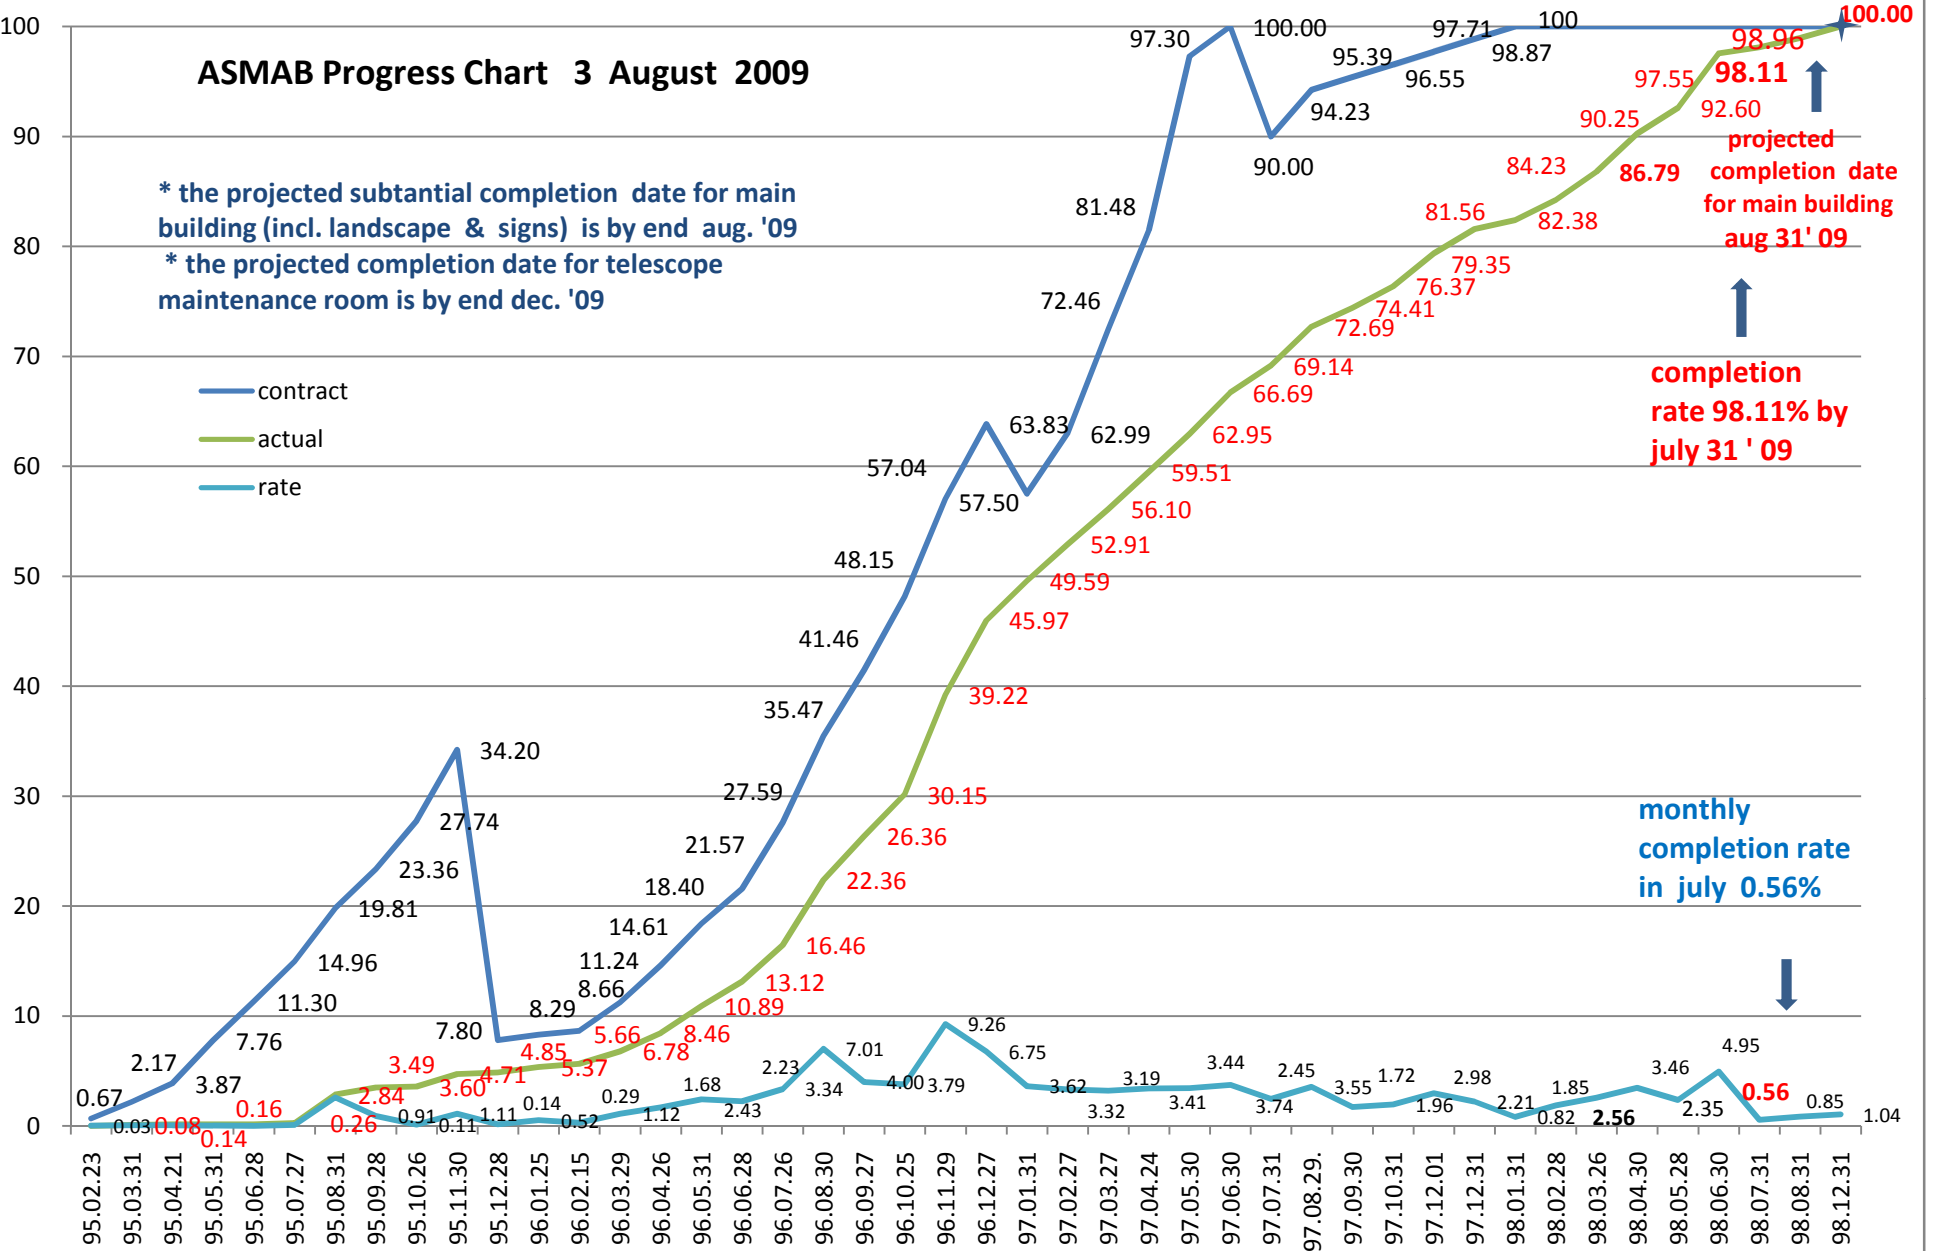

↑  
 projected completion date for main building aug 31 '09

↑  
 completion rate 98.11% by July 31 '09

↓  
 monthly completion rate in July 0.56%
